# **Budget Section**

## Senator Tony Grindberg, Chairman

### **December 13, 2011**

#### Department of Corrections and Rehabilitation

NDSP Building Project

Project Budget - \$64 million

Project Expenditures as of 11/30/11 – \$25.2 million

Significant Completion Date — December, 2012 (Demolition of East Cell House and West Security Fencing to be completed in Spring of 2013)

#### Project Scope:

New Administrative Segregation Unit – 108 Beds

New General Housing Unit – 180 Beds

New Intake / Orientation Unit – 120 Beds

New Medical Unit – 23 Beds

New NDSP Entrance / DOCR Administration Bldg.

New NDSP Warehouse

New South Guard Tower

**New Security Fencing** 

**Building Demolition:** 

East Cell House

**DOCR Administration Bldg** 

NDSP Warehouse

Warden's Residence

Deputy Warden's Residence


## oject Status:

Approximately 35% Complete

Remains On Budget / On Time




North Dakota State Penitentiary Entrance / DOCR Administration Bldg.

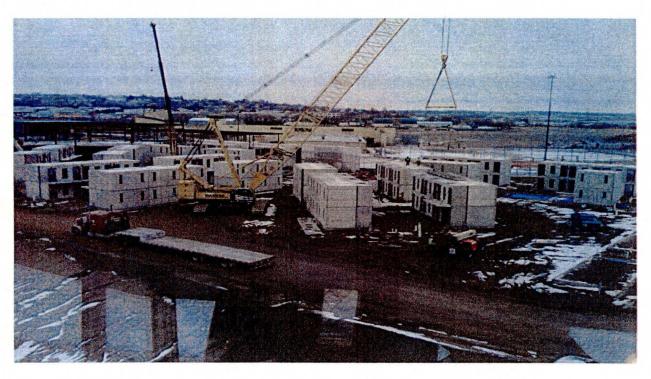


Precast Cell Houses (Looking NW – View from South Tower)



General Population Housing (Looking East – Interior View)

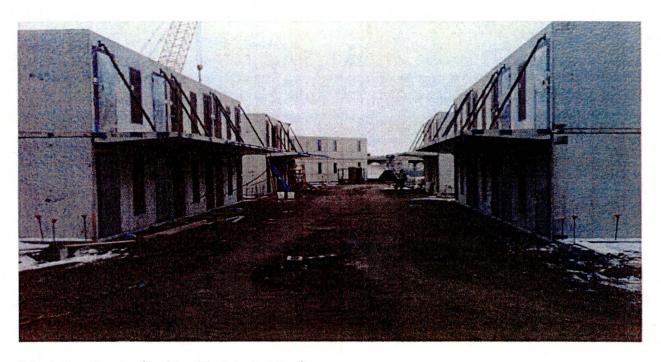

Orientation Housing (Looking SE – Interior View)

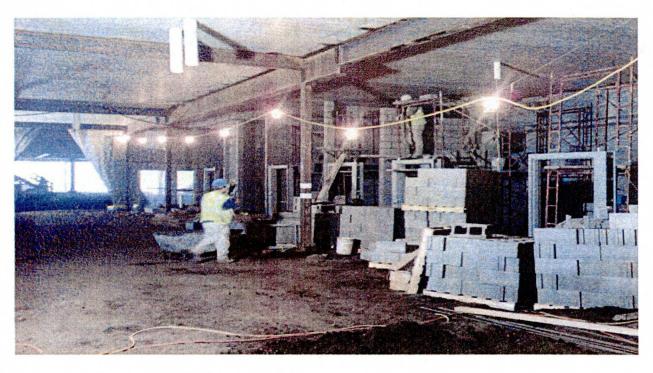

Medical Unit (Construction of Infirmary Cells)



Precast Cell Houses (Looking NW – Exterior View)



Setting Precast Cells (Looking West)
